Corporation of the Municipality of Thames Centre
4305 Hamilton Road, Dorchester, Ontario N0L 1G3 – Phone 519-268-7334 – Fax 519-268-3928 – www.thamescentre.on.ca – inquiries@thamescentre.on.ca

Municipality of Thames Centre

CONSTRUCTION UPDATE

King Street Storm Sewer Upgrade and Road Urbanization

November 10, 2026

Dear Property Owner / Resident,

The Municipality of Thames Centre (Municipality) hereby notifies and advises all residents and affected parties of the construction progress and update of the project **along King Street from Nissouri Road to Wye Creek Bridge**. A full-time inspector from WT Infrastructure Solutions Ltd., supported by periodic visits from our municipal staff, will continue to oversee the project to ensure everything runs as smoothly as possible. We're committed to keeping you informed and minimizing disruptions throughout this process.

Work Plan Staging– Please see attached map

Stage 1 Construction Update: Nissouri Road to Brooker Trail

- Storm sewer works – **Complete**
- Stringline for curb and gutter – **Complete**
- Curb and gutter installation – **Complete**
- Base asphalt installation – **Complete**
- Boulevard grading and sidewalk work - **Complete**
- Hydro One Pole Replacements – **Complete**
- Sod Installation – **Complete**
- Driveway restoration – **Complete**

Stage 1A (Deferred to early 2027): Nissouri Road and King Street Intersection

- Due to the required work in the intersection, Blue-Con requires a full intersection shut down. This work has been deferred to early 2027 to alleviate traffic concerns from surrounding construction projects.

Corporation of the Municipality of Thames Centre
4305 Hamilton Road, Dorchester, Ontario N0L 1G3 – Phone 519-268-7334 – Fax 519-268-3928 – www.thamescentre.on.ca – inquiries@thamescentre.on.ca

Stage 2 Construction Update: Brooker Trail to the Wye Creek Bridge

- Storm sewer works – **Complete**
- Stringline for curb and gutter – **Complete**
- Curb and gutter installation – **Complete**
- Base asphalt installation – **Complete**
- Boulevard grading and sidewalk work - **Complete**
- Hydro One Pole Replacements – **Complete**
- Sod Installation – **Anticipated completion November 13, 2026**

Stage 3: Final Restoration and Surface Asphalt

- Pedestrian crosswalk poles – **Anticipated installation the week of November 16, 2026**
- Topcoat Asphalt – **Anticipated November 11, 2026, weather pending**
- Line Painting – **Anticipated the night of November 11, 2026, contingent on asphalt placement**
- Road Reopening **– Anticipated November 13, 2026, contingent on asphalt placement**

If any mobility assistance is required, please do not hesitate to contact WT Infrastructure Solutions Inc. or the Municipality using the phone numbers or emails listed below. You can also speak directly to any construction worker wearing a white hard hat on-site.

Contact Information


The Municipality is dedicated to keeping you informed and supported throughout the construction process. Feel free to contact the Municipality or WT Infrastructure Solutions Inc. anytime with questions or concerns – we're here to assist you. Stay up to date on the Municipal Website: https://www.thamescentre.on.ca/KingStreetUpgrades26/

Municipality of Thames Centre
Tanner Stanton
(519) 268-7334 Ext. 235
tstanton@thamescentre.on.ca

WT Infrastructure Solutions Inc
Andrew Tulk
(519) 400-1185
andrew.tulk@wtinfrastructure.ca

After Hours Water Emergency Number: (519) 930-8118

KING STREET CONSTRUCTION - PROJECT STAGING

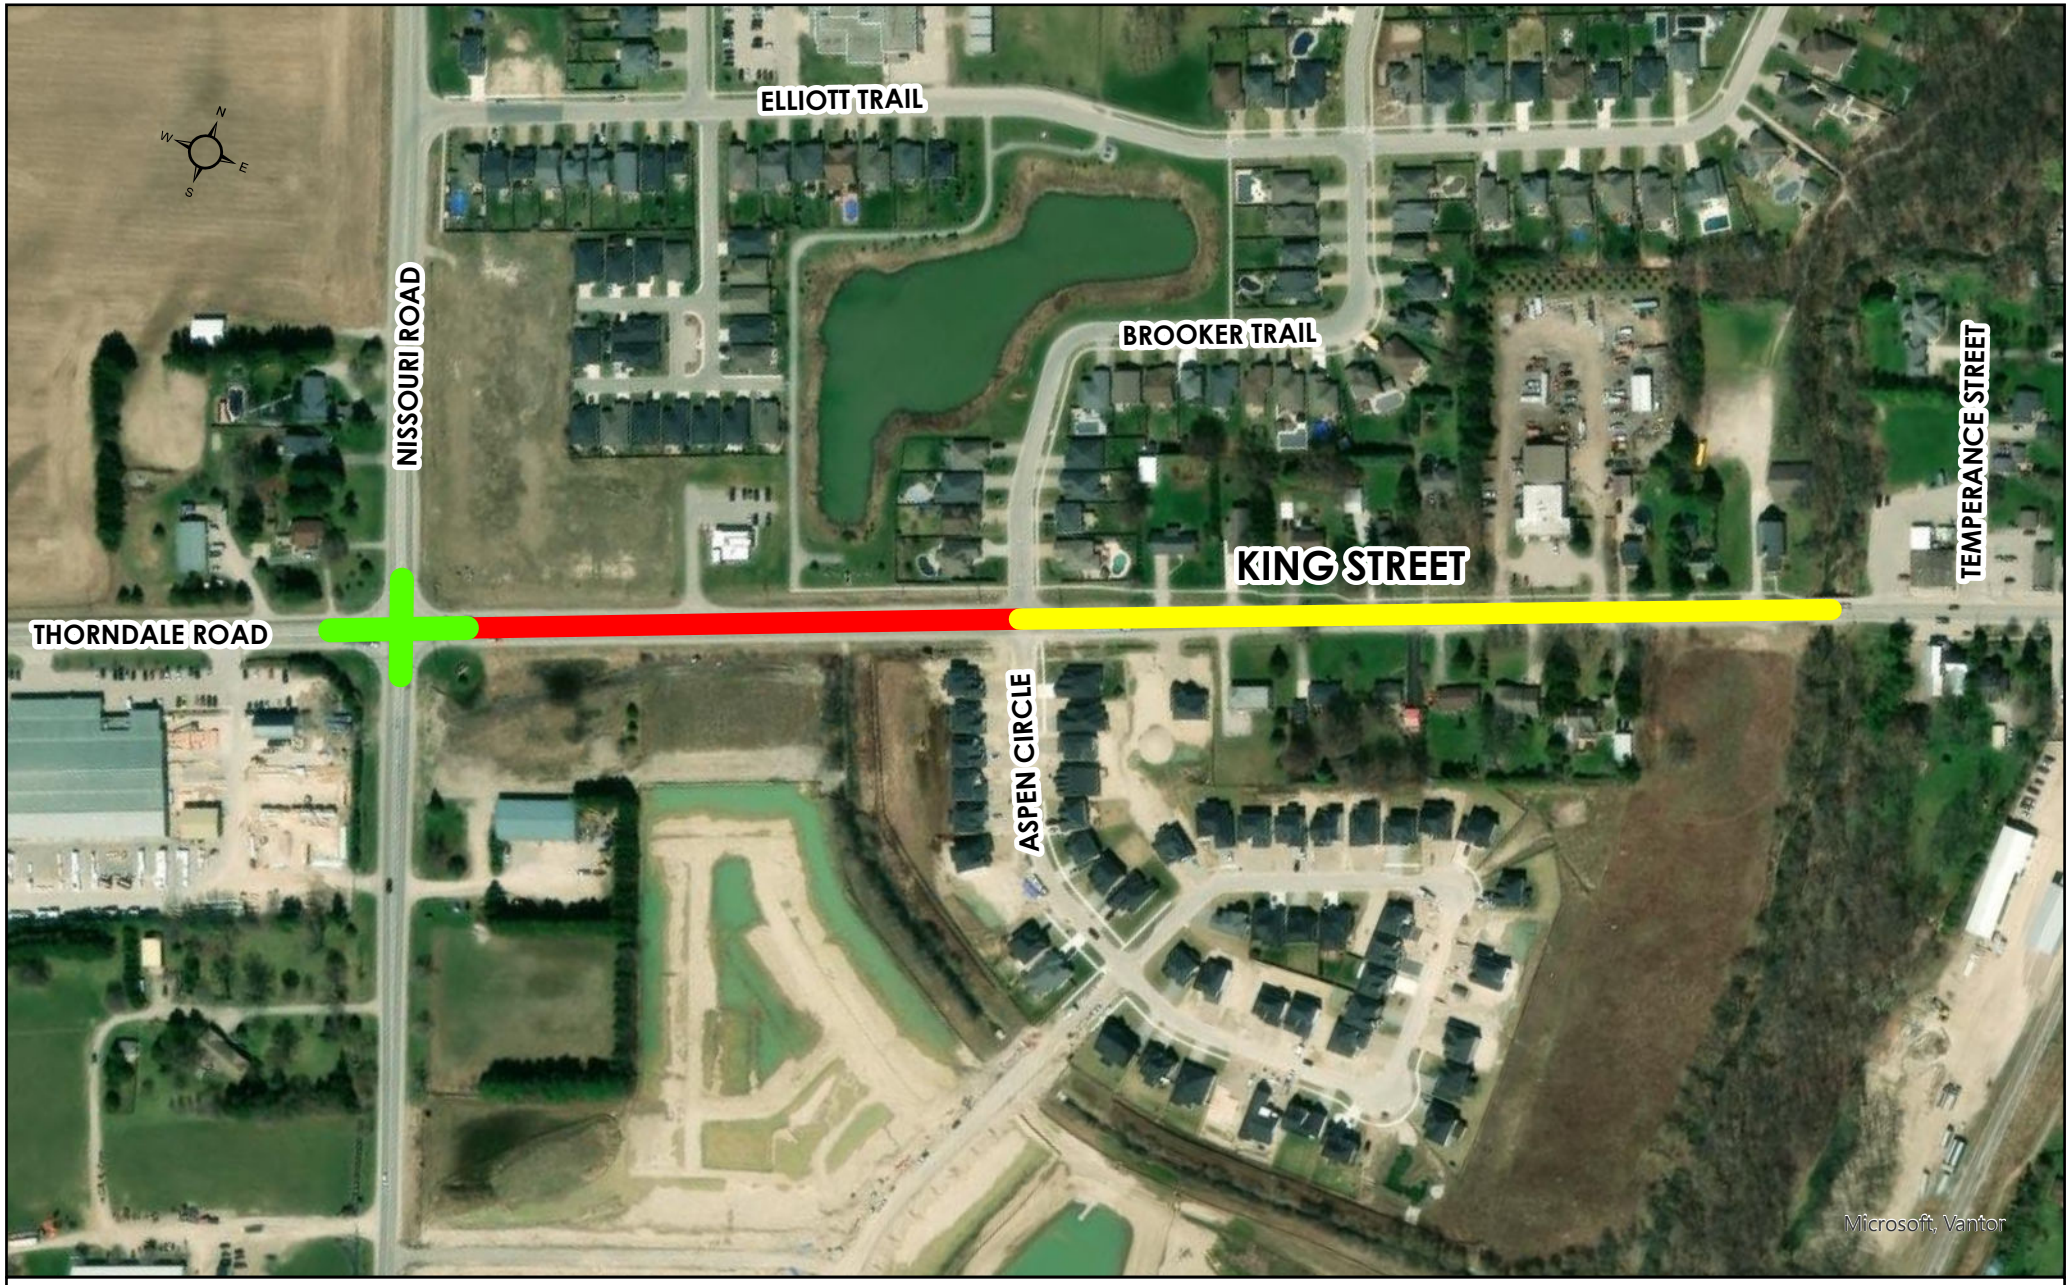

STAGE 1

STAGE 1A

STAGE 2

MUNICIPALITY OF Thames Centre
